



IMPACT Critical/Key Milestones

Baseline: January 31, 2004

Updated: 2/19/04


UID	ITEM	EVENT	2003		2004												Need Date	Total Slack
			N	D	J	F	M	A	M	J	J	A	S	O				
378	1	SWEA FM 1 Complete	12/8	▼													NA	Complete
485	2	SIT FM 1 HVPS Delivery to UMD	12/9	▼													NA	Complete
519	3	IMPACT Pre-Environmental Review (PER)			1/14	▼											NA	Complete
934	4	SEP Suite - 2nd EM I&T Pow Wow @ CIT			1/30	▼											NA	Complete
1155	5	Deliver SIT FM 1 Enclosure to UMD					3/16	▽									4/7/04	16 Days
498	6	MAG FM 1 Complete					3/29	▽									5/17/04	35 Days
482	7	SEP FM 1 LVPS Complete					4/6	▽									5/26/04	36 Days
381	8	SWEA FM 2 Calibration Complete					4/15	▽									7/20/04	67 Days
481	9	IDPU FM 1 LVPS Complete					4/23	▽									6/1/04	25 Days
489	10	SWEA FM 2 LVPS Complete					4/26	▽									7/12/04	53 Days
1160	11	Deliver SIT FM 1 Telescope to UMD					5/18	▽									6/10/04	16 Days
493	12	IDPU FM 1 Ready for Boom Suite I&T					5/21	▽									6/29/04	25 Days
1044	13	SIT FM 1 I&T Complete										6/21	▽				7/2/04	9 Days
963	14	SEP Suite - FM 1 I&T Complete										6/28	▽				7/9/04	9 Days
520	15	IMPACT Suite EMC Test Complete										7/12	▽				7/23/04	9 Days
471	16	Boom Suite - FM 1 Final I&T Complete										8/13	▽				10/6/04	37 Days
514	17	SWEA/STE-D IF FM 2 Complete										8/27	▽				9/28/04	20 Days
474	18	Integrated FM 2 Boom/IDPU I&T Complete										9/7	▽				10/5/04	20 Days
993	19	SEP Suite - FM 1 Environmental Tests										9/14	▽				10/6/04	16 Days
476	20	Boom Suite - FM 2 Final I&T Complete										9/28	▽				10/27/04	20 Days
179	21	SEP Suite - FM 2 Ready for Delivery to APL										10/12	▽				10/28/04	11 Days





IMPACT BOOM Master Schedule


Baseline: January 31, 2004

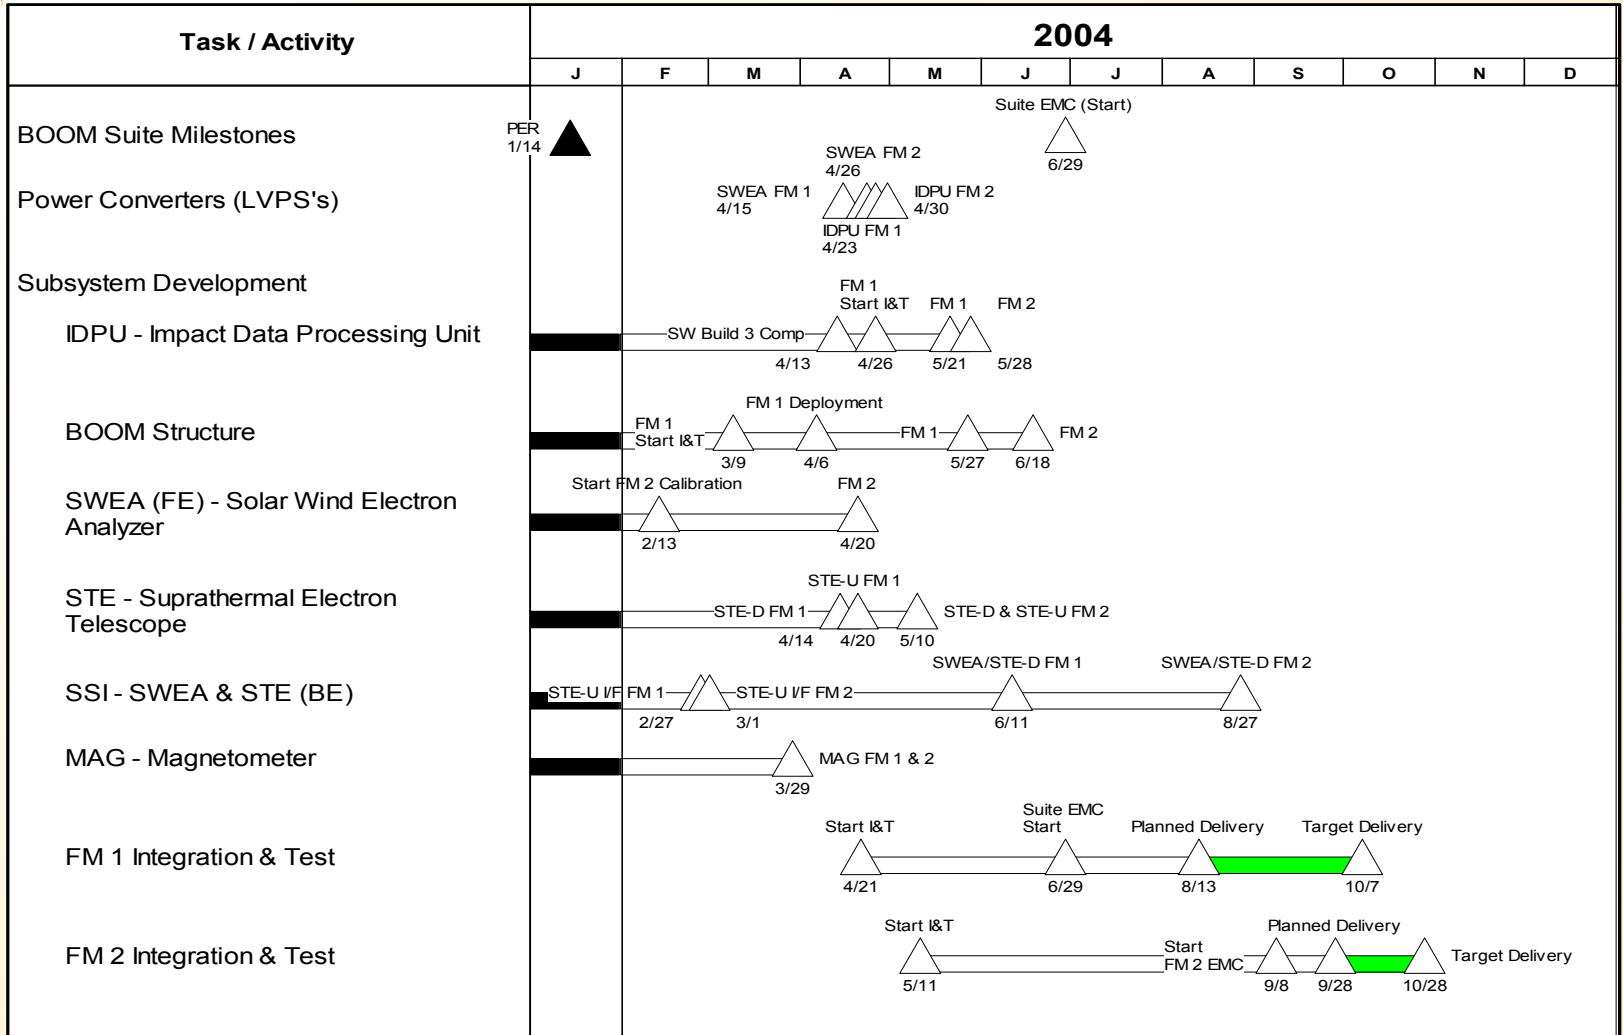




IMPACT SEP Master Schedule

Baseline: January 31, 2004

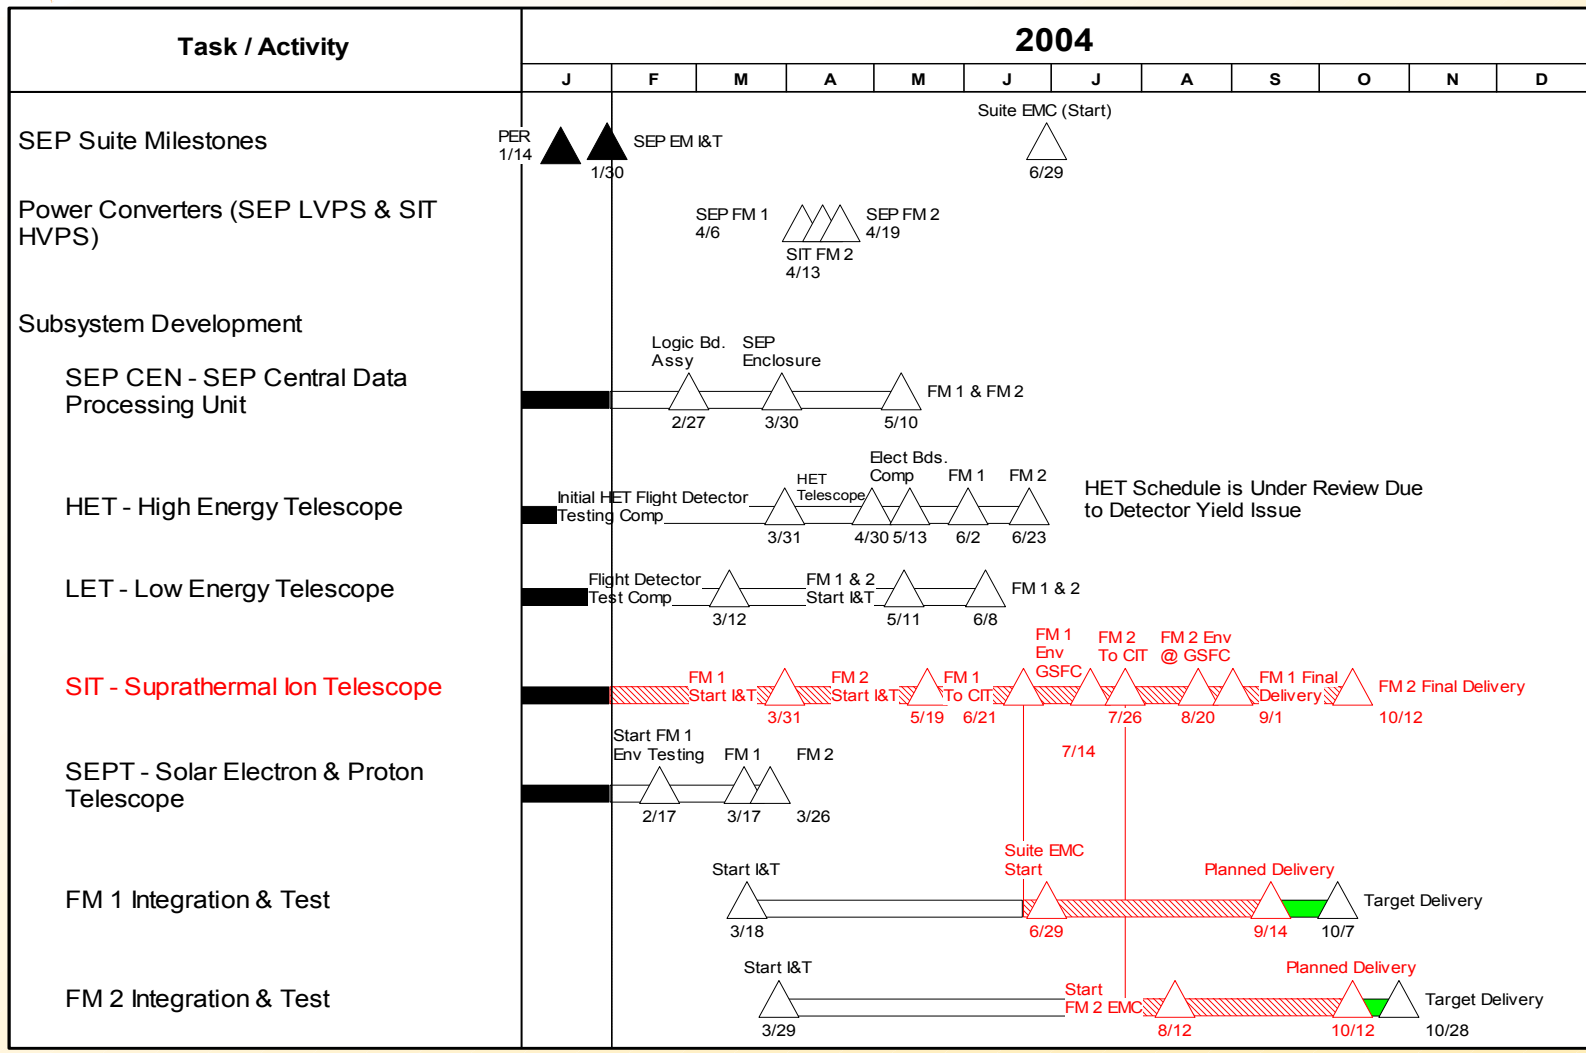



IMPACT Schedule Slack Trend (BOOM)

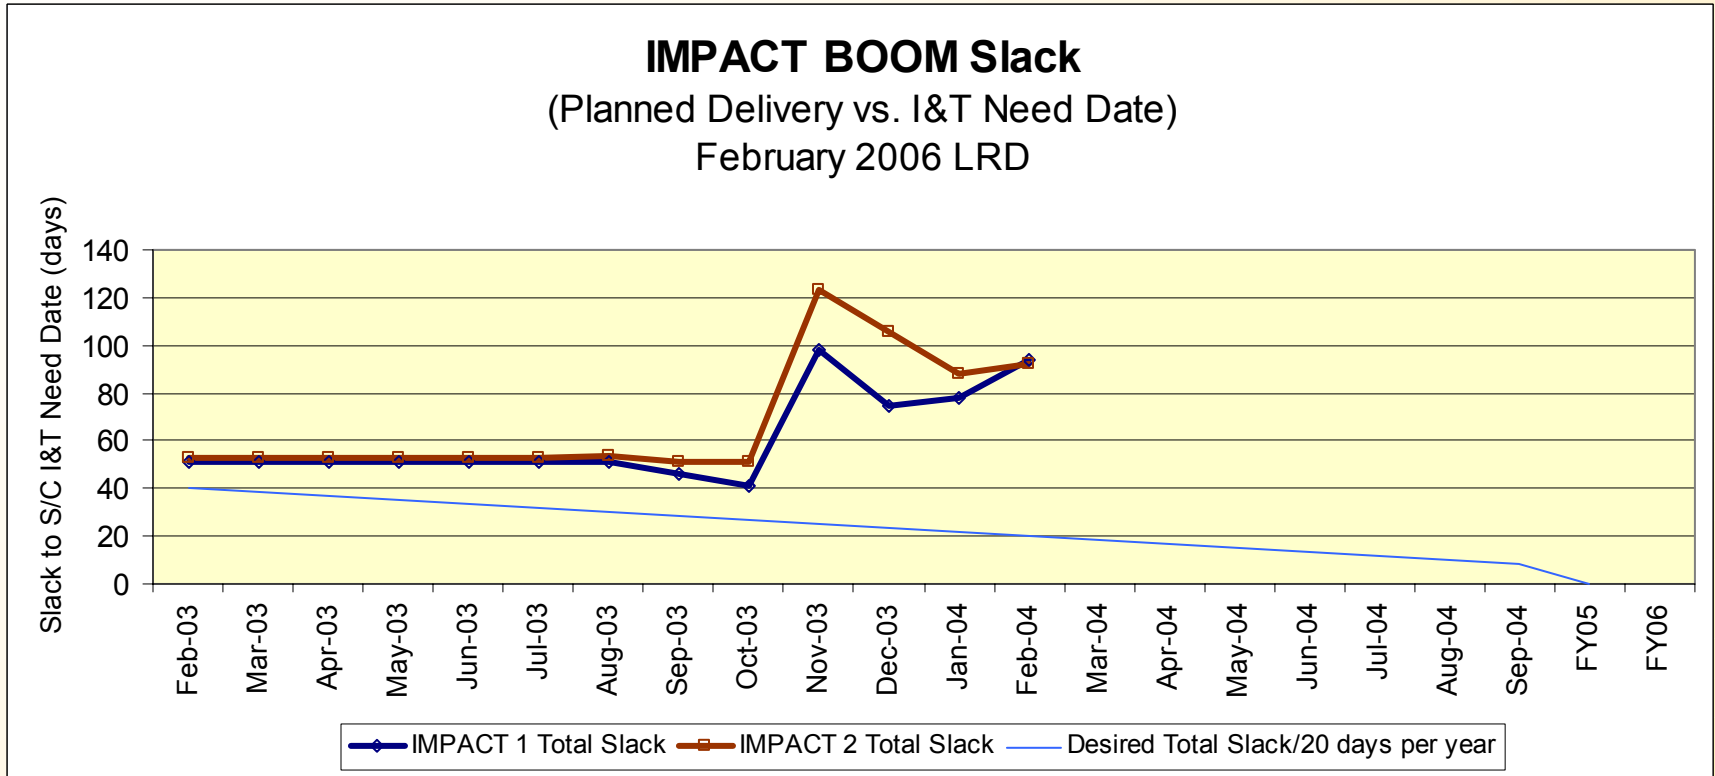


IMPACT 1 S/C I&T Need Date: 12/29/04
Planned Delivery Date: 8/13/04

IMPACT 2 S/C I&T Need Date: 2/10/05
Planned Delivery Date: 9/28/04





IMPACT Schedule Slack Trend (SEP)

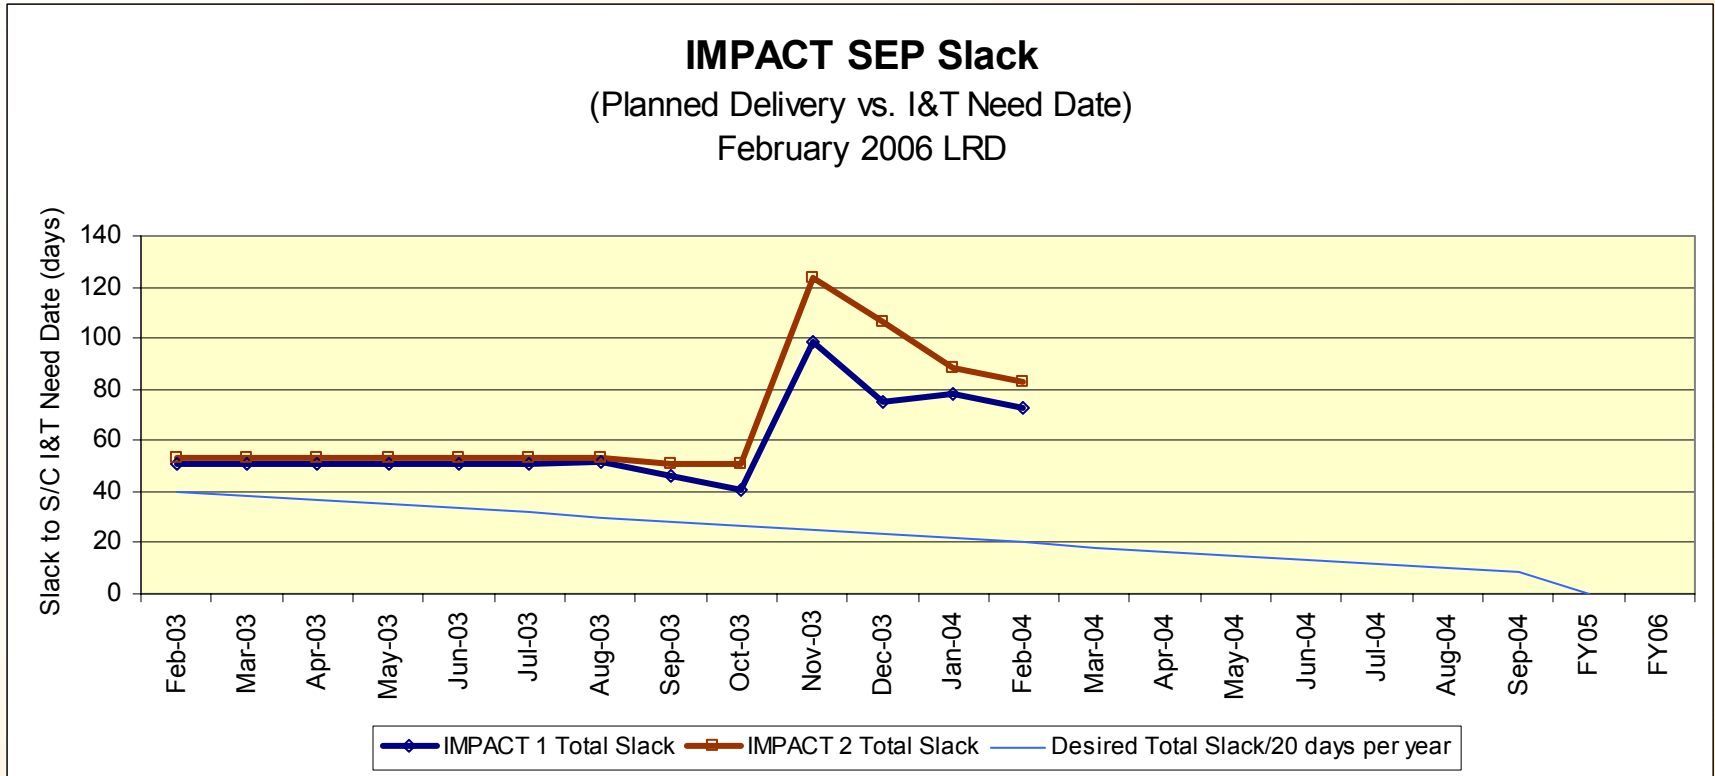

IMPACT 1 S/C I&T Need Date: 12/29/04
Planned Delivery Date: 9/14/04

IMPACT 2 S/C I&T Need Date: 2/10/05
Planned Delivery Date: 10/12/04

